

Your Company Name

Email: companyemail@mail.com
Phone: 978-555-1504

YOUR LOGO



Customer Information

1 Flatley Ave,
Manchester MA 01944,



MyRoofReport


Copyright © Offsite Roof Reports, LLC – All Rights Reserved www.MyRoofReport.com | (603)305-1456



Offsite Roof Reports, LLC accepts no liability for the content of this report, or for the consequences of any actions taken on the basis of the information provided | Report for Planning Purpose only. This report was prepared from historical imagery. **Please have all Information provided verified before placing order for Materials.** Aerial Image provided as a client courtesy. Please use your professional expertise when applying waste factor. Waste factor does not account for treatment of hips and ridges | See Website Disclaimer for further details



Total Roof Squares = 27.86			
-Waste Factor-			
10%	15%	20%	25%
30.65	32.04	33.43	34.82

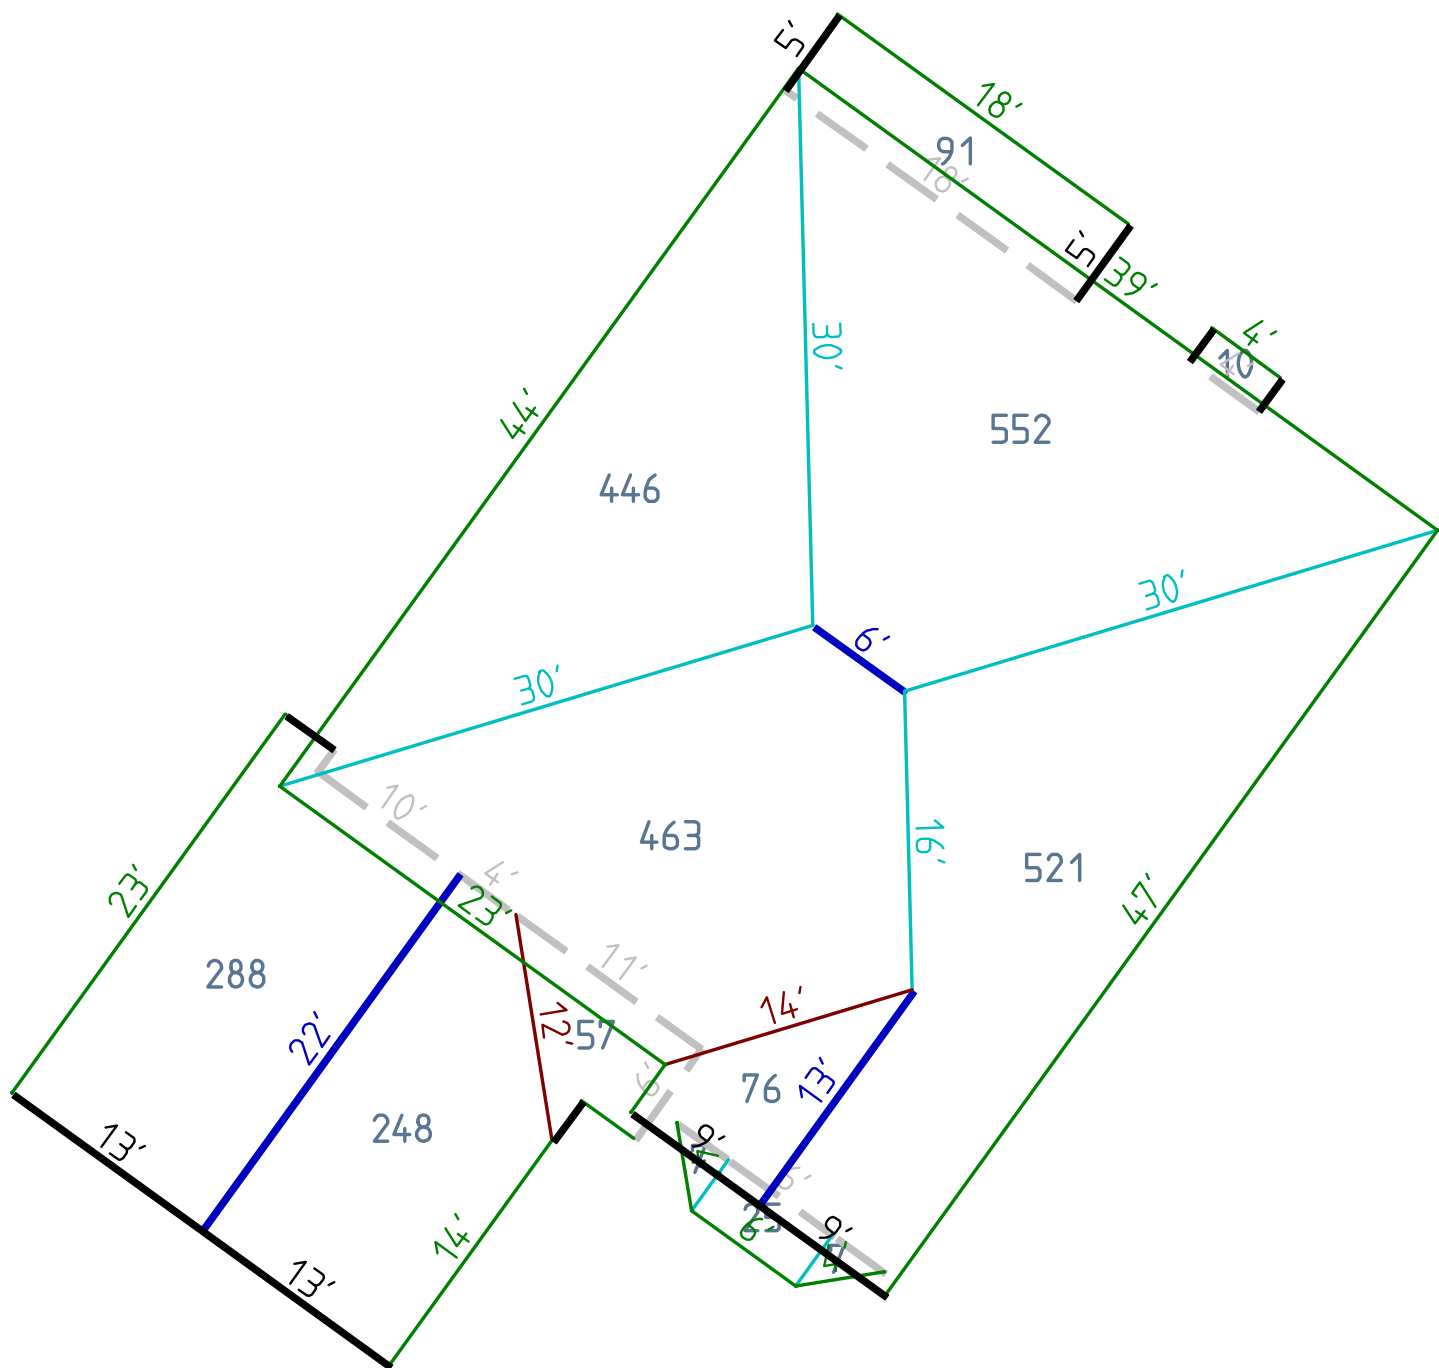

Total Quantities

Ridge Length=40'

Valley Lengths=26'

Hip Length=113'

Eave Length=233'


Rake Length=66'

Perimeter (Eave + Gable)=298'


Transition Length=0'

Step Flashing=28'

Apron Flashing=41'

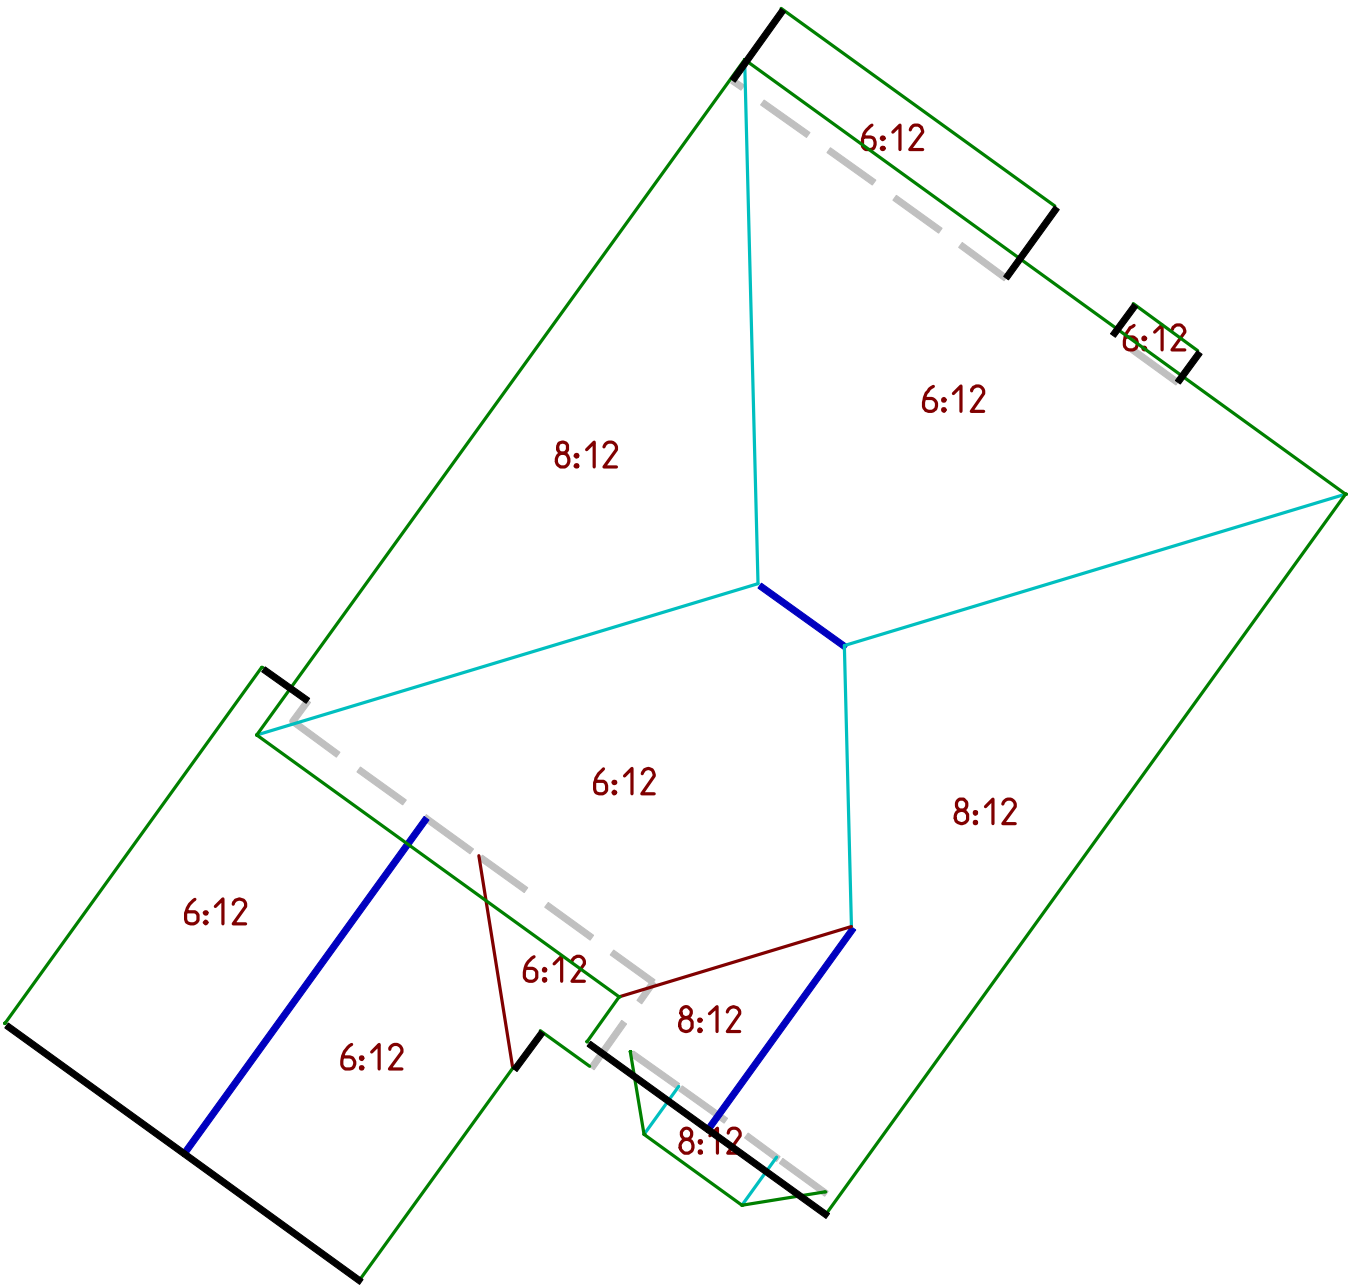

	6:12	8:12
Total Squares	17.06	10.80
Ridge Length (ft)	27'	13'
Eave Length (ft)	124'	108'
Hip Length (ft)	0'	113'
Valley Length (ft)	12'	14'
Gable Length (ft)	47'	19'
Step Flashing (ft)	20'	8'
Apron Flashing (ft)	34'	6'

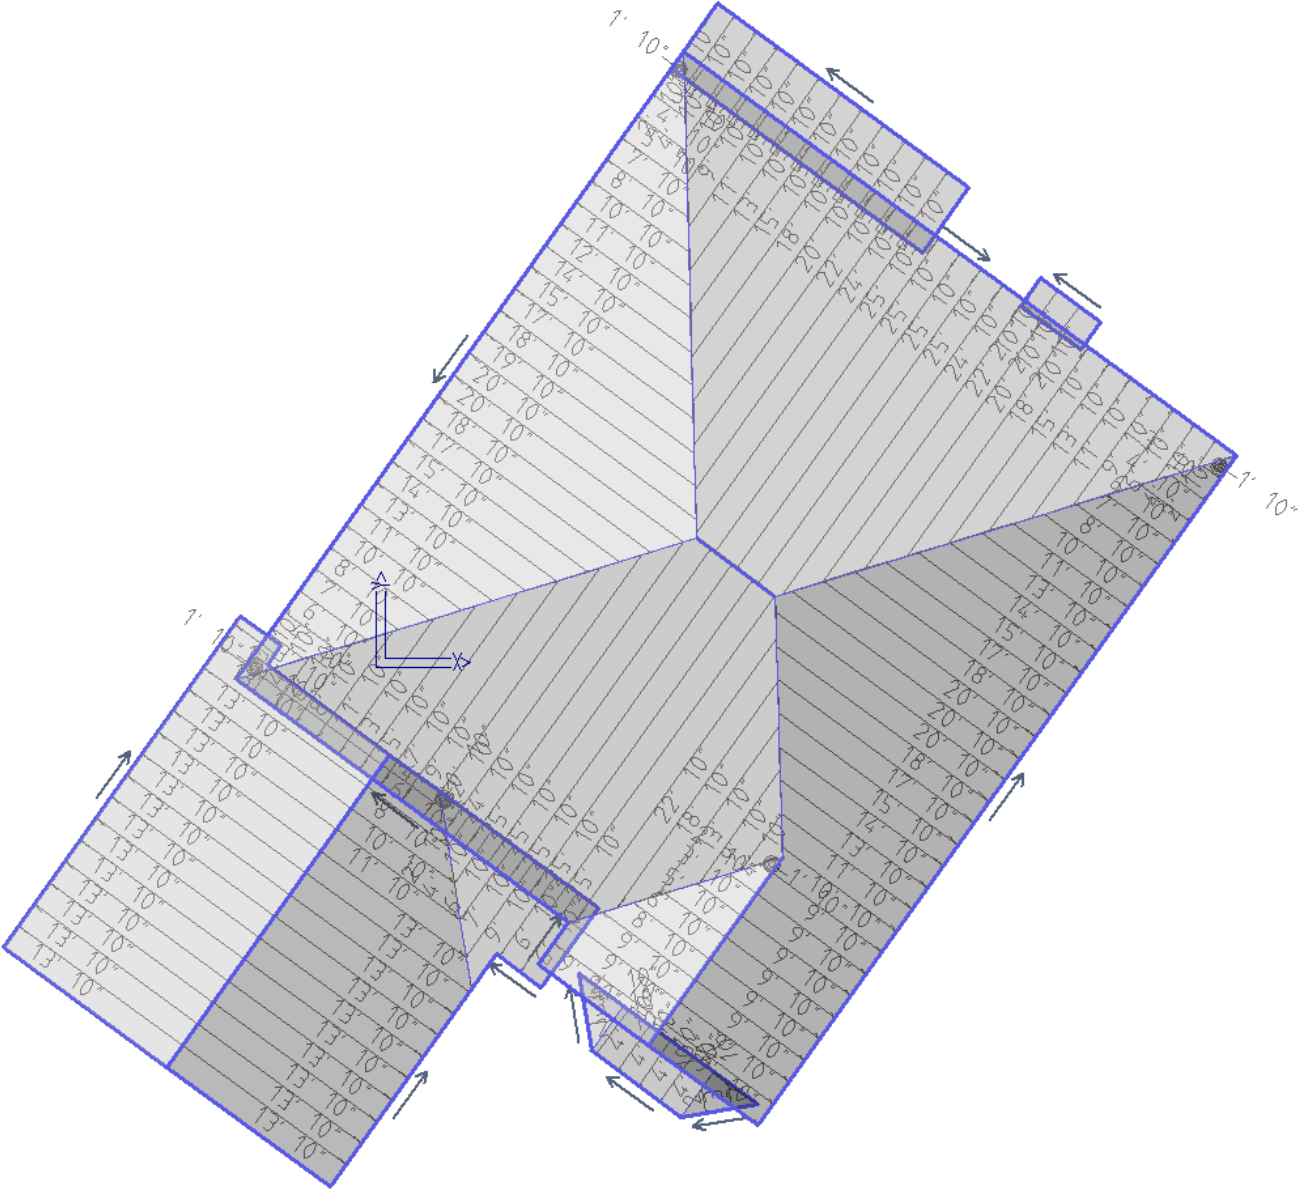

Standing Seam Panel Size	18"
Total Panel Length	2,085'
Sheet Area	31.27 sq
Roof Area	27.86 sq
Panel Area/ Roof Area Estimated Waste	11%
(Please use your professional expertise when applying waste factor)	
