Your Company Name

Email: companyemail@mail.com

Phone: 978-555-1504

YOUR LOGO

1 Flatley Ave Manchester MA 01944



Total Roof Squares = 24.17					
-Total Roof Waste Factor-					
10%	15%	20%	25%		
26.59	27.80	29.01	30.22		



MyRoofReport

Expert Roof Measurements

 $Copyright © Offsite Roof Reports, LLC - All \ Rights \ Reserved \\ \underline{www.MyRoofReport.com} \ | \ (603)305-1456$



Offsite Roof Reports, LLC accepts no liability for the any content of this report, or for the consequences of any actions taken on the basis of the information provided | Report for Planning Purpose only. This report was prepared from historical imagery. Please have all Information provided verified before placing order for Materials. Aerial Image provided as a client courtesy. Please use your professional expertise when applying waste factor, including Suggested waste factor for planning purpose only we accept no liability. See Website for further details

Ridge Length=20'

Eave Length=178'

Transition Length=0'

Valley Lengths=0'


Rake Length=15'


Step Flashing=5'

Hip Length=93'

Perimeter (Eave +Gable)=193'

Apron Flashing=78'

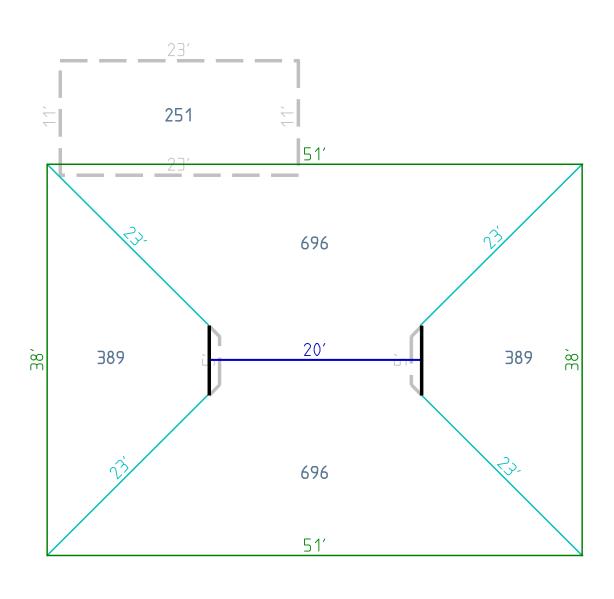

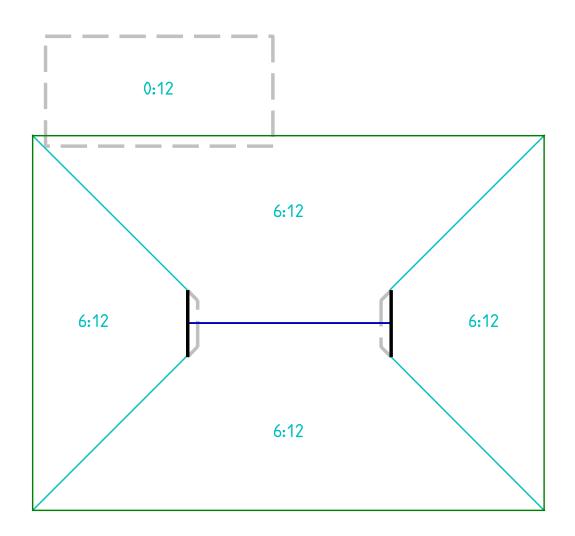

Shingle (6:12) Total Squares = 21.66					
Shingle Waste Factor					
10%	15%	20%	25%		
23.83	24.91	26.00	27.08		

Material Breakdown

Total Squares	Shingle (6:12) 21.66	Flat 2.51
Ridge Length (ft)	20'	0'
Eave Length (ft)	178'	0'
Hip Length (ft)	93'	0'
Valley Length (ft)	0'	0'
Gable Length (ft)	15'	0'
Step Flashing (ft)	5'	0'
Apron Flashing (ft)	11'	68'
Eave Length (ft) Hip Length (ft) Valley Length (ft) Gable Length (ft) Step Flashing (ft)	178' 93' 0' 15' 5'	0' 0' 0' 0' 0'
